# **HRA Capital Projects**





## **Update for Tenants Forum**

**November 2013** 



Cost Centre	Project	Budget £000
H420	Improving Access for Disabled People	458
H430	Decent Homes - Electrical Upgrades	208
H435	Decent Homes - Kitchen & Bathroom Renewal	318
H440	Door Entry Systems	50
H441	Window Renewal	146
H442	Central Heating Upgrades	297
H443	Roof Renewal	250
H445	Descent Homes-External Wall Repairs	40
H446	External Doors	214
H447	Voids Repairs and Improvements	350
H448	Structural Improvements	164
H449	External Insulation	110
H450	Environmental Improvements – Highfield Road	40
H455	Decent Homes - Replace Oil Tanks	38
H456	Decent Homes - Fire Precautions	70
H457	Decent Homes - Other works	40
H458	Internal Wall Insulation	29
H459	Car Park Enhancements	45
H460	Conversion of Warden's House	60
H461	Hampden Crescent - Regeneration	150
H462	Decent Homes - Fire Precautions	108
H463	Homes for the Future	75
TOTAL		3260

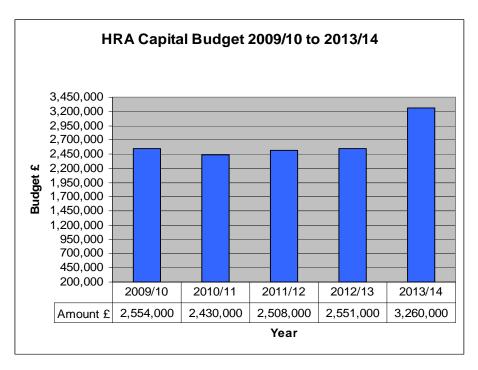

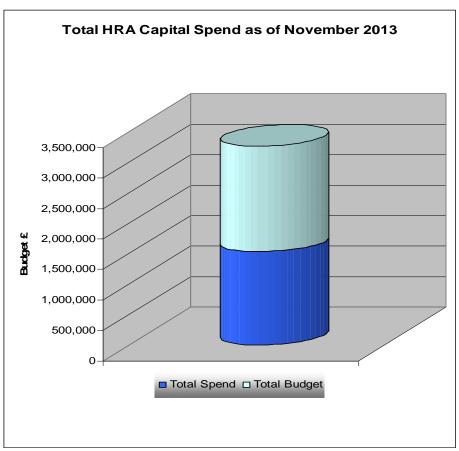

Total HRA Capital Budget 2013/14 £3,260,000

Total spend as of November 2013 £1,527,000

Name	H420 – Improving Access for Disabled People			
Description	Installation of aids and adaptations to council housing.			
Location	Various			
Status	On-site		Units	65
Contractor	KBC Environmental C	are		-
Cost		Now	Last	
Information	Budget	£458,000	£458,000	
	Actual spend to date	£133,644	£112,200	
	Projected spend	£458,000	£458,000	
Programme Information		Now	Last	
mormation	Brief	-	-	
	Sketch scheme	-	-	
	Tender approval	-	-	
	Start on site	-	-	
	Completion	-	-	
Comments	38 properties completed by the end of October. On target to complete all 65 units within budget by year end.			

Name	H430 – Decent Home	H430 - Decent Homes - Electrical Upgrades			
Description	Rolling programme to upgrade electrical installations.				
Location	Various				
Status	On-site		Units	89	
Contractor	KBC Environmental C	are			
Cost		Now	Last		
Information	Budget	£208,000	£208,000		
	Actual spend to date	£76,477	£65,000		
	Projection	£208,000	£208,000		
Programme		Now	Last		
Information	Brief	-	-		
	Sketch scheme	-	-		
	Tender approval	-	-		
	Start on site	-	-		
	Completion	-	-		
Comments	•	23 units completed to date. Rewires delayed due to other commitments. It is intended to complete as many units as			

Name	H435 – Kitchen and Bathroom Renewal			
Description	Rolling programme of kitchen and bathroom refurbishments.			
Location	Various			
Status	On-site		Units	32
Contractor	KBC Environmental C	are	•	_
Cost		Now	Last	
Information	Budget	£318,000	£318,000	
	Actual spend to date	£240,023	£195,000	
	Projection	£318,000	£318,000	
Programme Information		Now	Last	
iniormation	Brief	-	-	
	Sketch scheme	-	-	
	Tender approval	-	-	
	Start on site	-	-	
	Completion	-	-	
Comments	Completed 23 units by complete all units with		•	)

Name	H440 - Door Entry Sy	rstems		
Description	A rolling programme to install door entry systems to blocks of flats.			
Location	Kettering Albert Street; Alexandra Street; Alfred Street; Arthurs Way; Barnes Close; Fishton Close; Gloucester Close; Highfield Crescent; Highfield Road; Thorngate Street.			
Status	On-site		Units	169
Contractor	Entrotec			
Cost		Now	Last	
Information	Budget	£50,000	£50,000	
	Actual spend to date	£26,613	£26,549	
	Projected spend	£50,000	£50,000	
Programme		Now	Last	
Information	Brief	Jan-13	Jan-13	
	Sketch scheme	Feb-13	Feb-13	
	Tender approval	N/A	N/A	
	Start on site	Aug-13	Aug-13	
	Completion	Mar-14	Mar-14	
Comments	1 block completed. 9 programming units to		•	nd 18

Name	H441 – Window Rene	ewal			
Description	A rolling programme for windows.	A rolling programme for the installation of replacement UPVC windows.			
Location	Kettering George Street; Walnut Crescent Broughton St Andrews Court sheltered scheme Burton Latimer Spring Gardens; Yeoman's Court kitchen and laundry. Loddington Main St				
Status	On-site Units 32			32	
Contractor	Astraseal				
Cost		Now	Last		
Information	Budget	£146,000	£146,000		
	Actual spend to date	£77,168	£44,133		
	Projected spend	£76,000	£76,000		
Programme		Now	Last		
Information	Brief	N/A	N/A		
	Sketch scheme	Dec-12	Dec-12		
	Tender approval	Apr-13	Apr-13		
	Start on site	May-13	May-13		
	Completion	Dec-13	Dec-13		
Comments	works at Yeoman's Co	St Andrews Court and Spring Gardens are complete. Further works at Yeoman's Court are to be tendered with a view to completion within budget this year.			

Name	H442 – Central Heating Upgrades			
Description	Rolling programme central heating boiler replacements.			
Location	Various			
Status	On-site		Units	156
Contractor	KBC Environmental C	are		
Cost		Now	Last	
Information	Budget	£297,000	£297,000	
	Actual spend to date	£150,875	£107,000	
	Projection	£297,000	£297,000	
Programme Information		Now	Last	
IIIIOIIIIalioii	Brief		-	
	Sketch scheme		-	
	Tender approval		-	
	Start on site		-	
	Completion		-	
Comments	Completed 131 units t within budget by year	•	o complete all	units

Name	H443 – Roof Renewa	1		
Description	Replacement of tiled roofing.			
Location	Kettering Almond rd; Centre Parade; Ivy Rd; Myrtle Road; Orchard Crescent Flats.			
Status	On-site		Units	55
Contractor	Warkton Roofing			
Cost		Now	Last	
Information	Budget	£250,000	£250,000	
	Actual spend to date	£68,769	£15,438	
	Projected spend	£220,000	£220,000	
Programme		Now	Last	
Information	Brief	N/A	N/A	
	Sketch scheme	N/A	N/A	
	Tender approval	May-13	May-13	
	Start on site	Aug-13	Aug-13	
	Completion	Mar-14	Mar-14	
Comments	Work commenced in A end of October. On table by year end.	•	•	•

Name	H445 – Decent Home	es – External Wall	Repairs		
Description	Brickwork repairs to various properties in the Borough.				
Location	<b>Kettering</b> The Oval				
Status	On-site		Units	30	
Contractor	KBC Environmental C	are	•		
Cost		Now	Last		
Information	Budget	£40,000	£40,000		
	Actual spend to date	£34,176	£27,000		
	Projection	£40,000	£40,000		
Programme		Now	Last		
Information	Brief	-	-		
	Sketch scheme	-	-		
	Tender approval	-	-		
	Start on site	-	-		
	Completion	-	-		
Comments	Completed 22 propert behind last month due complete all units on be	to adverse weathe	er, but will catc		

Name	H446 – External Doo	H446 – External Doors			
Description	Rolling programme of external door replacements.				
Location	Various				
Status	On-site		Units	256	
Contractor	KBC Environmental C	are			
Cost		Now	Last		
Information	Budget	£214,000	£214,000		
	Actual spend to date	£138,236	£130,000		
	Projection	£214,000	£214,000		
Programme		Now	Last		
Information	Brief	-	-		
	Sketch scheme	-	-		
	Tender approval	-	-		
	Start on site	-	-		
	Completion	-	-		
Comments	Originally planned to f be fitted in 2013/14. 2 2013. On target to co	283 units installed b	y the end of O	ctober	

Name	H447 – Void Repairs	and Improvement	:s	
Description	Major repair works to void properties.			
Location	Kettering Almond Road; Barnes Close; Highfield Road; Walnut Crescent; Whiteford Drive. Barton Seagrave Polwell lane Broughton Wellingborough Road Desborough Hilltop Pytchley Isham Road. Rothwell Cambridge Street.			
Status	On-site		Units	50
Contractor	A L Holland			
Cost		Now	Last	
Information	Budget	£350,000	£350,000	
	Actual spend to date	£225,538	£194,001	
	Projected spend	£350,000	£350,000	
Programme		Now	Last	
Information	Brief	N/A	N/A	
	Sketch scheme	N/A	N/A	
	Tender approval	Jun 10	Jun 10	
	Start on site	Apr-13	Apr-13	
	Completion	Mar-14	Mar-14	
Comments	Works completed to 1 further 10 on budget b		rget to comple	te a

Name	H448 – Structural Im	provements		
Description	Ad hoc underpinning and damp proofing works.			
Location	Kettering Almond Road; Ash Road; Elizabeth Road; Highfield road; Judith Road; New Buildings; Stamford Road; Walnut Crescent; Weekley Glebe; Windmill Avenue Barton Seagrave Castle Way Broughton Wellingborough road Burton Latimer Pioneer Avenue Desborough Alexandra Road; Mansfield Close Loddington Main Street Rothwell Daisybank; Hawkins Close; Meadow Road Thorpe Malsor The Square Willbarston Queens Close.			
Status	On-site		Units	82
Contractor	Various			
Cost		Now	Last	
Information	Budget	£164,000	£164,000	
	Actual spend to date	£90,591	£85,178	
	Projected spend	£164,000	£164,000	
Programme		Now	Last	
Information	Brief	N/A	N/A	
	Sketch scheme	N/A	N/A	
	Tender approval	N/A	N/A	
	Start on site	Apr-13	Apr-13	
	Completion	Mar-14	Mar-14	
Comments	Works completed to 2 further 10 on budget b		cast to complet	te a

Name	H449 – External Insulation				
Description	Installation of external wall insulation on properties without mains gas.				
Location	Broughton Wellingborough Road. Pytchley Isham Road				
Status	On-site		Units	16	
Contractor	Goldsmith and Son		•		
Cost		Now	Last		
Information	Budget	£110,000	£110,000		
	Actual spend to date	£93,831	£25,671		
	Projected spend	£95,000	£95,000		
Programme		Now	Last		
Information	Brief	Feb-13	Feb-13		
	Sketch scheme	Apr-13	Apr-13		
	Tender approval	May-13	May-13		
	Start on site	Jul-13	Jul-13		
	Completion	Mar-14	Mar-14		
Comments	Works completed to 8 properties. Grant funding of £39,000 from Scottish Power has been obtained under the ECO scheme. Stage two has now commenced with an additional £40,000 ECO funding due on completion. On target to complete 16 units within budget by year end.				

Name	H450 – Environmental Improvements – Highfield Road				
Description	New recycling and bin	areas to three bloc	cks of flats.		
Location	Kettering Whiteford Drive blocks	s 2-4b and 6-12b.			
Status	Consultation		Units	18	
Contractor	N/A				
Cost		Now	Last		
Information	Budget	£40,000	£40,000		
	Actual spend to date	£0	£0		
	Projected spend	£45,000	£45,000		
Programme Information		Now	Last	_	
mormation	Brief	Feb-13	Feb-13		
	Sketch scheme	Mar-13	Mar-13		
	Tender approval	Dec-13	Dec-13		
	Start on site	Feb-14	Feb-14		
	Completion	Mar-14	Mar-14		
Comments	Section 20 procedure now underway. Tender process to commence January 2014.				

Name	H455 – Decent Homes – Replace Oil Tanks					
Description	Replacement of centra	Replacement of central heating oil tanks in rural properties.				
Location	Various					
Status	Complete		Units	12		
Contractor	KBC Environmental C	are				
Cost		Now	Last			
Information	Budget	£38,000	£38,000			
	Actual spend to date	£28,126	£18,000			
	Projection	£38,000	£38,000			
Programme		Now	Last			
Information	Brief		-			
	Sketch scheme		-			
	Tender approval		-			
	Start on site		-			
	Completion		-			
Comments	12 units replaced to date. An additional 2 units have also been installed, giving a total of 14 units. All installations completed within budget. Currently inspecting condition of a further 10 tanks which may be added to the project.					

Name	H456 – Decent Homes – Fire Precautions					
Description	Replacement of timb	er fire doors in flats	with GRP door	rs.		
Location	Various	Various				
Status	Tender stage		Units	72		
Contractor	Permador					
Cost		Now	Last			
Information	Budget	£70,000	£70,000			
	Actual spend to date	£4,820	£4,483			
	Projected spend	£54,000	£54,000			
Programme Information		Now	Last			
information	Brief	Sep-12	Sep-12			
	Sketch scheme	Nov-12	Nov-12			
	Tender approval	May-13	May-13			
	Start on site	Nov-13	Nov-13			
	Completion	Mar-14	Mar-14			
Comments	Tender awarded for £54,000. Start date November 2013. On target to complete 72 units within budget by year end.					

Name	H457 – Decent Hom	H457 – Decent Homes – Other Works				
Description	Miscellaneous works properties.	to address potentia	lly non-decent			
Location	Kettering 129 Barnwell Street Rothwell 44, 46 and 48 Underwood Road					
Status	Complete		Units 4			
Contractor	A L Holland					
Cost		Now	Last			
Information	Budget	£40,000	£40,000			
	Actual spend to date	£33,791	£28,624			
	Projected spend	£40,000	£40,000			
Programme		Now	Last			
Information	Brief	Feb-13	Feb-13			
	Sketch scheme	May-13	May-13			
	Tender approval	Jul-13	Jul-13			
	Start on site	Aug-13	Aug-13			
	Completion	Mar-14	Mar-14			
Comments	All four properties now completed within budget.					

Name	H458 – Internal Wall Insulation			
Description	Provision of wall and I	oft insulation to inc	rease energy e	efficiency.
Location	N/A			
Status	Complete		Units	30
Contractor	SIG Energy Managem	nent		
Cost		Now	Last	
Information	Budget	£29,000	£29,000	
	Actual spend to date	£11,499	£9,802	
	Projected spend	£9,802	£9,802	
Programme		Now	Last	
Information	Brief	N/A	N/A	
	Sketch scheme	N/A	N/A	
	Tender approval	N/A	N/A	
	Start on site	N/A	N/A	
	Completion	N/A	N/A	
Comments	All work was completed in 2012/13. Two payments made in 2013/14 for work completed later in year. Remaining budget is to be reallocated.			

Name	H459 – Car Park Enhancements			
Description	Resurfacing/repairs t parks.	o garage courts and	I sheltered hou	sing car
Location	<b>Kettering</b> Windsor Gardens Sh	eltered Scheme		
Status	Tender (stage 1) awa	arded	Units	74
Contractor	Boothville Construction	on		
Cost		Now	Last	
Information	Budget	£45,000	£45,000	
	Actual spend to date	£345	£345	
	Projected spend	£45,000	£45,000	
Programme		Now	Last	
Information	Brief	Aug-13	Aug-13	
	Sketch scheme	Sep-13	Sep-13	
	Tender approval	Oct-13	Oct-13	
	Start on site	Nov-13	Nov-13	
	Completion	Dec-13	Dec-13	
Comments	Work commencing at Windsor Gardens w/c 04/11/13. (Contract awarded for £14,000.) Stage 2 (Alexandra Street) to be tendered.			

Name	H460 – Conversion of Warden's House			
Description	Conversion of warden users.	's house to provide	2 flats for whe	elchair
Location	Kettering The Lawns sheltered s	scheme.		
Status	Complete		Units	2
Contractor	Boothville Constructio	n		•
Cost		Now	Last	
Information	Budget	£60,000	£60,000	
	Actual spend to date	£51,189	£51,189	
	Projected spend	£51,189	£51,189	
Programme		Now	Last	
Information	Brief	2011	2011	
	Sketch scheme	Feb-13	Feb-13	
	Tender approval	Mar-13	Mar-13	
	Start on site	Apr-13	Apr-13	
	Completion	Sep-13	Sep-13	
Comments	Works completed in September 2013 – on programme and £12,000 below budget.			

Name	H461 – Hampden Crescent - Regeneration			
Description	Refurbishment of two improvements.	blocks of flats and	environmental	
Location	Kettering Hampden Crescent			
Status	Feasibility stage		Units	169
Contractor	N/A			
Cost		Now	Last	
Information	Budget	£150,000	£150,000	
	Actual spend to date	£20,596	£0	
	Projected spend	£150,000	£150,000	
Programme		Now	Last	
Information	Brief	May-12	May-12	
	Sketch scheme	N/A	N/A	
	Tender approval	N/A	N/A	
	Start on site	N/A	N/A	
	Completion	N/A	N/A	
Comments	Designs prepared and circulated to tenants in September.			

Name	H462 – Decent Home	es – Fire Precautio	ons		
Description	Various remedial works identified during fire risk assessments.				
Location	Kettering Barnes Close; George Street; The Lawns sheltered scheme; Whiteford Drive.				
Status	On-site		Units	169	
Contractor	Smiths Fire				
Cost		Now	Last		
Information	Budget	£108,000	£108,000		
	Actual spend to date	£19,053	£17,922		
	Projected spend	£108,000	£108,000		
Programme		Now	Last		
Information	Brief	Jul-11	Jul-11		
	Sketch scheme	Sep-11	Sep-11		
	Tender approval	Mar-13	Mar-13		
	Start on site	May-13	May-13		
	Completion	Mar-14	Mar-14		
Comments	Stage 1 (Barnes Cl. and Whiteford Dr.) complete. Stage 2 (George St. and Saunders Cl.) commenced Sep 13 and due for completion in Oct/Nov. Tenders for stage 3 (The Lawns) now returned. Contract awarded to Boothville Construction for £22,624.				

Name	H463 – Homes for the Future			
Description	Refurbishment of pre- energy efficient homes		provide safe, modern,	
Location	<b>Desborough</b> 5 Addison Road			
Status	Feasibility stage		Units	
Contractor	N/A			
Cost		Now	Last	
Information	Budget	£75,000	£75,000	
	Actual spend to date	£0	£0	
	Projected spend	£75,000	£75,000	
Programme		Now	Last	
Information	Brief	N/A	N/A	
	Sketch scheme	N/A	N/A	
	Tender approval	N/A	N/A	
	Start on site	N/A	N/A	
	Completion	N/A	N/A	
Comments	Project on hold pending approval of 'Homes for the Future' proposals.			
