East Kettering Liaison Forum

Project Update

19th June 2014

Adrian Arnold KBC



General Project Update

- Timeline for Delivery
 - Project Plan, Route Map and Timeline
- Planning Applications
 - Primary School (PS4)
 - Variation of Condition Application Tranche 2 (Alledge Brook)
 - Hallam Variation of Condition Application
 - Pre-Commencement Conditions
 - Residential Applications Hallam, Taylor Wimpey, Persimmon
- Infrastructure Update
 - Infrastructure Overview
 - Highway Works and Start Times
 - J10/10A Business Case
 - Weekley/Warkton Avenue



Timeline for Delivery

 Committee Programme – July 8th & 23rd, September 4th & 9th, October 7th & 14th

Updated Timeline – KBC

Project Plan / Route Map – ABL



	ttering		1			Contraction of the local sectors in the local secto			1		
Work		April	May	June	July	August	September	October	November	December	
lannie	8 s105 (Hallam, Taylor Wimpey & Persimmon)	complete 1106 with TW, Hallam & Persimmon (ABL signed 09/13)			target to conclude						
	Final pre development conditions				all pre development conditions discharged						
	Specific detailed condition discharge pre development			ly house builder on individual pa	CONTRACTOR OF THE OWNER						
1	RMA (Infrastructure) Access D		MMA and ACK. Associated	see delivery							
A	RMA (I) attenuation for 1st dwellings		RMA approved	see delivery							
	RMA (I) Access E plus 500m road		All sugar succession	see delivery							
	RMA (I) road from central park to school (& Cranford Rd to school)					and the second second	- Income and the second se		(Carport of Carport of	delivery May to June & July t September 2015	
5	RMA Access F plus 1,000m road		MAR and AOK approved	see delivery							
D	RMA (I) P54 (first primary school)	(I) P54 (first primary school) RMA submission Consultation co				see delivery					
r.	RMA FW (By AWSL)	Reconvertion B.	design sentenwriting	Design		Yes.	planning submittion	committee	see delivery		
	RMA DWH/Barratt (R7, R9, R10)		RMA approved	see delivery							
G	RMA Persimmon(R23 & R26)			detailed layout.			committee date??	delivery			
н	RMA TW (R19)	detailed application		RMA submission		BMA committee??	Land dr	swdown		And Descent strength	
1	RMA ABL (R20, R24, E3, DC2)				and a second	delivery					
A	Attenuation Basin		Newta licent	ce and removie	Frelim & prep	s104 tech approvel and agreement	01/09/14 contract commence 15 weeks			surface water solution available 30/10/14	
	Access E and S00 m road								discound-		
	250 m road through to Central Bowl										
	Central Bowl to school										
	Access F and 300 m road		freim Suter	ADJOR-14	1778/118	CHON BEREOVAN	Access	(warm	#14 micers	A B access	
	ext 600m road								stil mail (28 seeries)		
	Cranford Rd to school										
	ichool PS4		school package tendered		tender return 21 July	tender comparison & pre contract period			Construction of PS	4 school and playing fields	
6] I	oul Water strategic sol"n		1					strategic main upgrade			
	eccess D and roads					DIVH commence made	87.89.810 access		delivery		
	WH house building							DWH NO	un building		
81	ther house builders commence							- 1	Potential Personnon star		
stee		- SA - S - S	1.				10	and the second second			
< I	fistict Centre			Bran	ideng			matket	ung of DC		
	ne Loan Funding		a standing the provincent agreed			-	-				
						tor Access 8 works	-				
	(P					Junia	d talaama bata jaabiist ay waxa	and the second s			
	CA LSIP CA LIF school			infrastructure contract agreed							
-	and a second second		infrastructure contract agreed	with HCA					and an inclusion of the second second	THE Arrest A and start to contra	
H	CA LIF non school		WIRD HCA						A statement of the second second	AUGS Access & and estad to centra	
23	1		and the second second							1	
ways	corridors										
	d Access F								A TANTA TARTALANS INCOME.		

FEMALONCIA IN LODGED

Kettering Borough Council

Atread on 10/06/2014 # 15/21


ast Kettering						2	015					
Work - Description	January	February	March	April	May	June	July	August	September	October	November	December
lianning	1	Sector A	1000			1000						
s106 (Hallam, Taylor Wimpey Persimmon)	4								1			
Final pre development condit	lons											
Specific detailed condition			And in case of the local division of the loc		and the second second							
discharge pre development RMA (Infrastructure) Access 0		1	1				1		1	1	-	
RMA (I) attenuation for 1st												-
dwellings					1							
RMA (I) Access E plus 500m ro RMA (I) road from central par												
school (& Cranford Rd to scho												1.200.000
RMA Access F plus 3,000m ro	bd											
D RMA (I) PS4 (first primary scho	iol)											
E. RMA FW (By AWSL)												
RMA DWH/Barratt (R7, R9, R1	0)			5 A			112					
G RMA Persimmon(R23 & R26)	-	-										
H RMA TW (R19)		delivery					-		-		-	-
		or with								-		
3 RMA ABL (R20, R24, E3, DC2)	-	-										
A Attenuation Basin					1							N.
Access E and 500 m road	All second s	disease in the local disease i	19410									
250 m road through to Central			delivery									
Bowl	Address (Constant)		distant.		- In the second second	delivery						
Central Bowl to school								delivery				
Access F and 300 m road	delivery											
next 600m road	1			HZE:	acesa		delivery			L		
Cranford Rd to school							Searchited 4	ted for he below	Unk road completed			
D School PS4							contingency period	snagging	PS 4 swallable for 01/09/15		-	
Foul Water strategic sol"n												
		T.										
Access D and roads	Party and a state of the state	Concernance -										
DWH house building	attenuation available	occupation										
H & J Other house builders commen	Potential TW start		Potential R24 start									
et stages	-				Df2.arcen			_				delivery to benefit fro
Distict Centre			legali					DC2 delivery				
ĸ		MMA DO2 81			committee (2223)							
1					,	marketing private health and cat	at OCIWITH benefit of Smill acce	H.		legate		
1							KMA DO	1 or 2 pr		committee		
o Prime Loan Funding												
SEMLEP												
NEP	Ward NEE for southing state	Constant Companying and California	ET Condition I made at Access 4									
HCA LSIP					I DO DO TO	States of States and States	drast 1980 for money and road h	stream of a liter state & stream				
HCA UF school			draw for	school								
HCA LIF non school									1			
IN UP IN SCHOOL											L	
IES:						(h and a second s	1	English and the second		
hways corridors												
ton Road Access F												
ton Road Access E												

Presid == 14/06/2014 at 1221



EK Route Map 2014-15

Highways Corridors v. 13.06.14

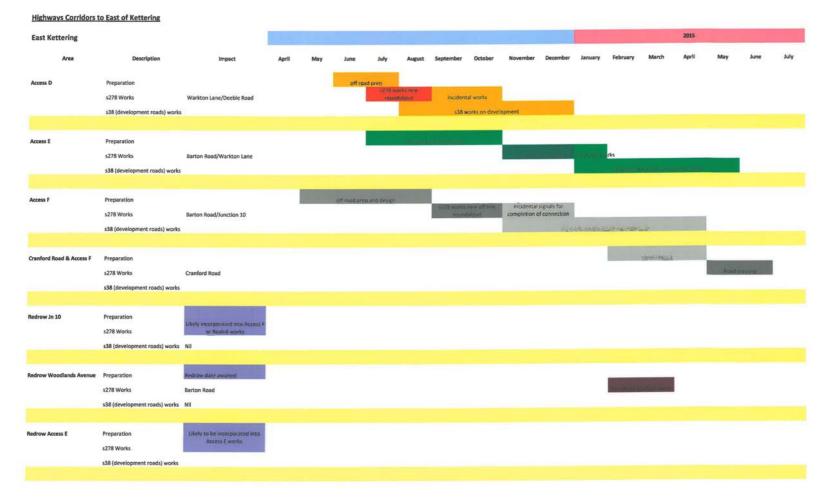


Page 1 of 1




Planning Applications: Primary School

- ◆ Aim to open for Sept 2015 earlier than required.
- Funded time limited concentrated delivery period, funding has to be spent/committed by March 2015
- Brings forward other parcels close to District Centre.
- Enables the link up of roads through to the site to take place earlier.
- A primary school will still be delivered early.
- Safe routes to school will still apply.



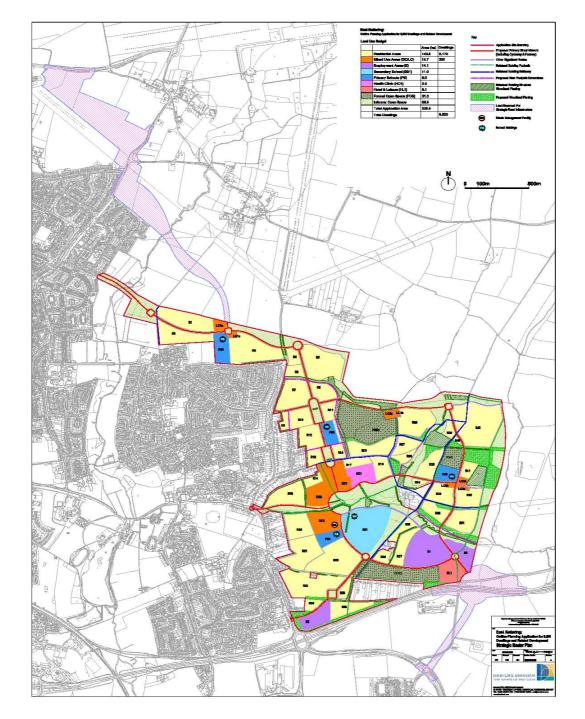



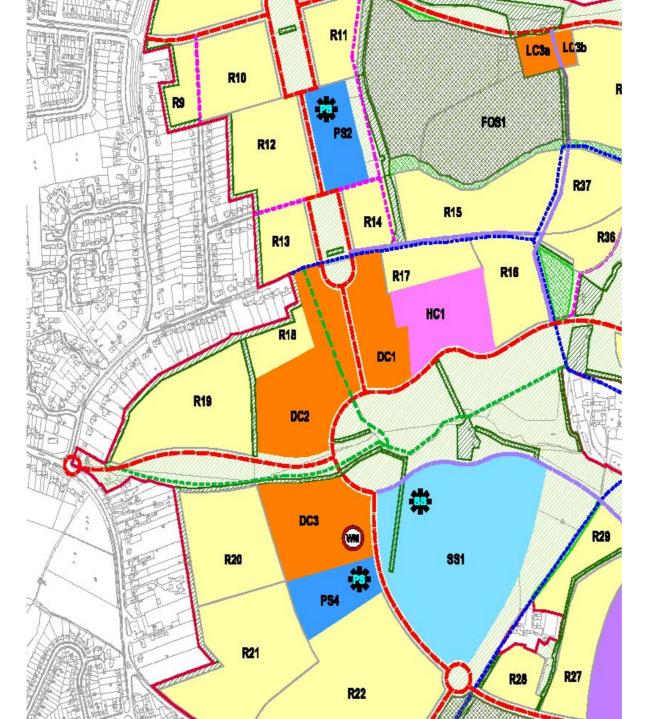














ScalegA1: As indicated Date: 28.04.14

Dwy Noi (SK)04 Revi C



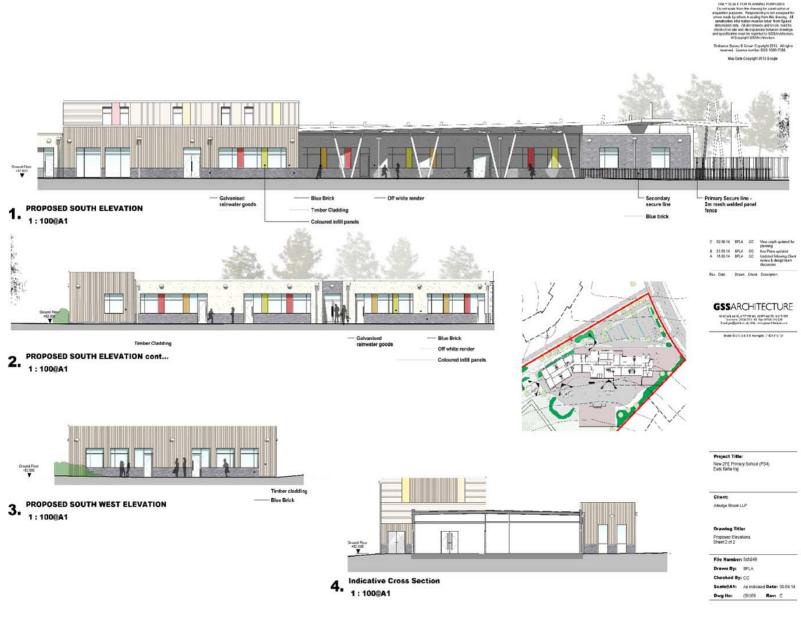





3D View 1 rev A

PS4 – NEW 2FE PRIMARY SCHOOL





Variation of Condition Application 2 (VOC2)

This VOC2 seeks to:

- Vary the Strategic Master Plan, Phasing Plans and Land Use Schedule
- Amend the phased approach from 3 Phases of development to 2 Phases
- Amend the trigger point from 1750 to 2700 dwellings for the conditions requiring highway improvements at junctions 10 and 10A
- Amend the 300 review trigger to 375



Hallam Variation of Condition

- Condition 18 Code for Sustainable Homes
- Condition 19 Lifetime Homes
- Condition 22 Interim Design Stage Assessment Cert.
- Condition 42 Access to A14 (300)
- Condition 45 Removal of road improvements (c) Deeble Road/Windmill Ave : now covered by Hallam draft S106



Pre-Commencement Conditions

Strategic Landscaping – awaiting additional information

Ecological Management Plan – approved (SUDS/Road)

 Prior to development of parcel – to be submitted by Alledge Brook or individual house builders.



Residential Applications

- David Wilson Homes/Barratts (parcels R7, R9 and R10 accessed off Deeble Road/Warkton Lane Junction)
 - Hallam S106 final draft
 - Pre-commencement and reserved matters conditions currently being looked at by DWH
 - Start on site anticipated Summer 2014
- Taylor Wimpey (parcel R19 accessed off Barton Road/Warkton Lane Junction)
 - Current Full Application is to be changed to a Reserved Matters
 - Due in end of June possible committee September/October
- Persimmon (parcels R23 and R26 site is located south of Cranford Road).
 - On-going discussions regarding layout and house types
 - Removal of balancing pond
 - Increase in no. of units to 320 from 308




Infrastructure

- Infrastructure Overview
- Highway Works and Start Times
- Junction 10/10a Business Case
- Weekley Warkton Avenue
- Roxhill possible committee 23rd July




EK Route Map 2014-15

Highways Corridors v. 13.06.14

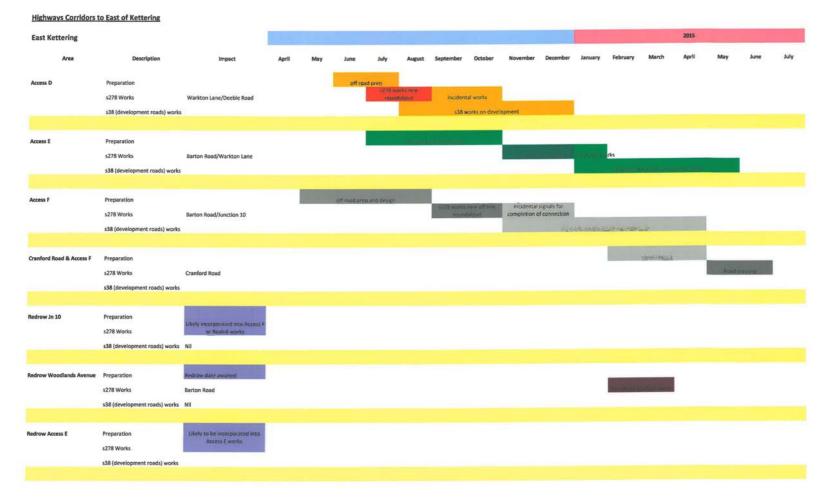


Page 1 of 1




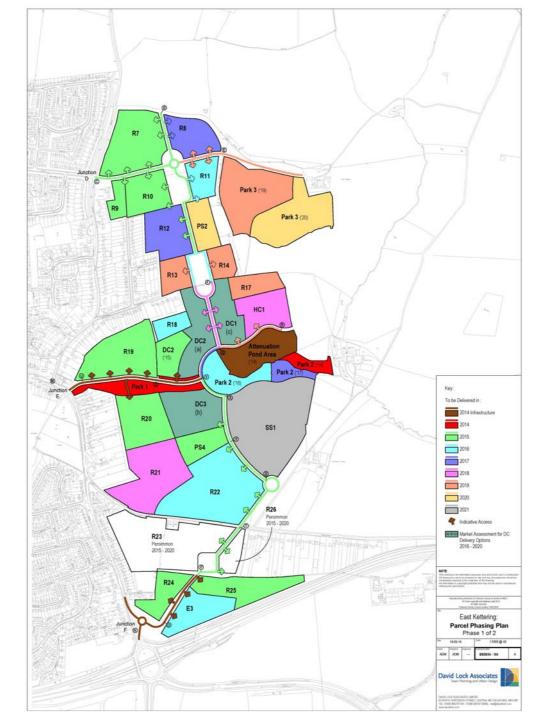



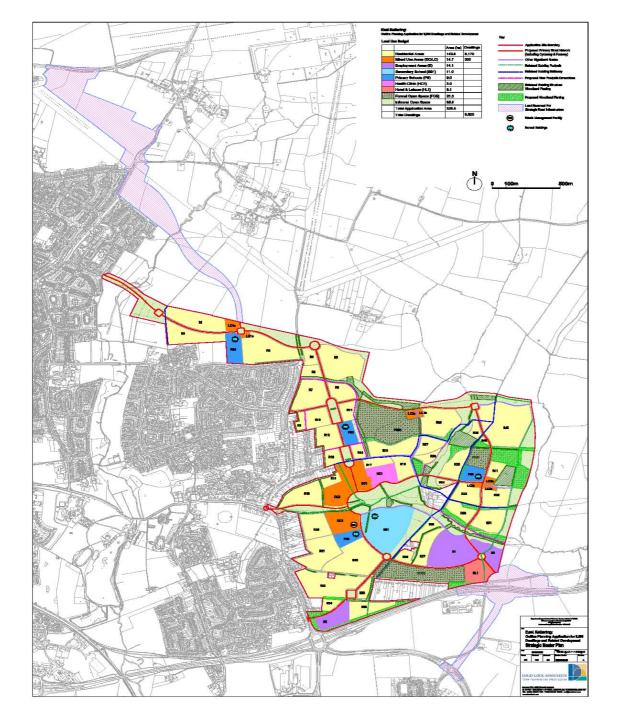




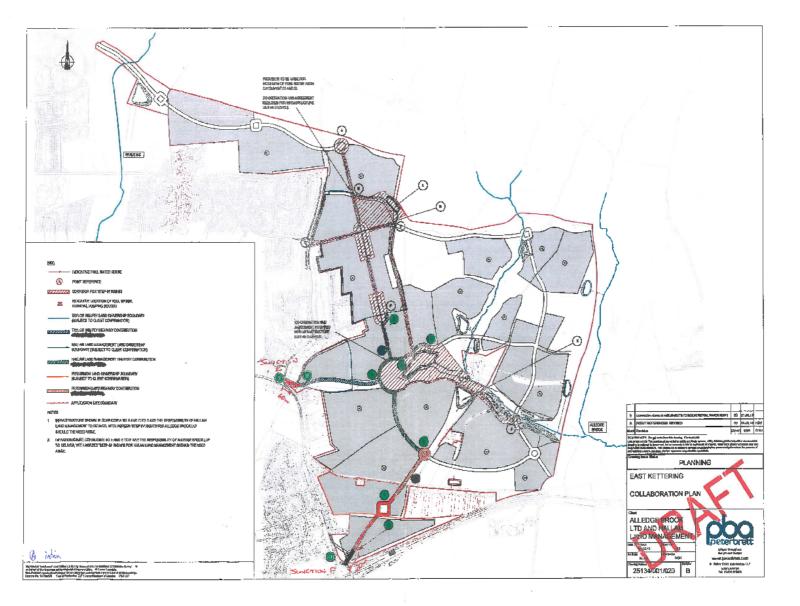




Roxhill Site Plan

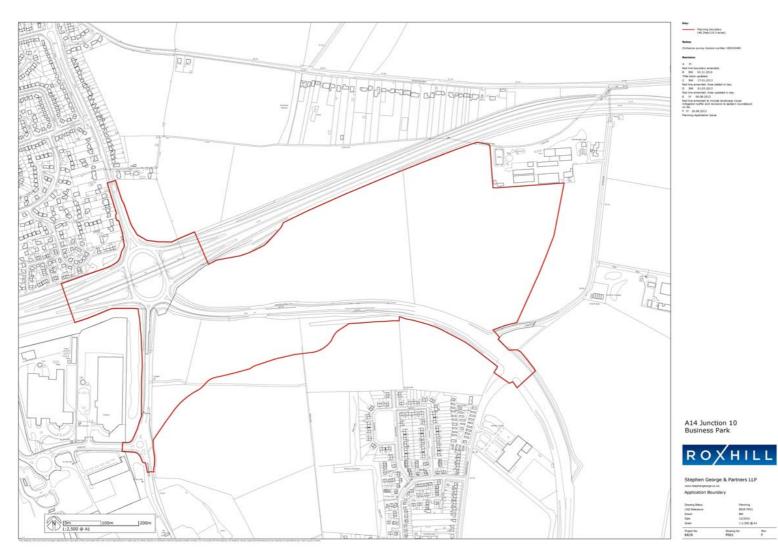



Roxhill Masterplan

ROXHILL^{AT} J10 Business Park • Kettering

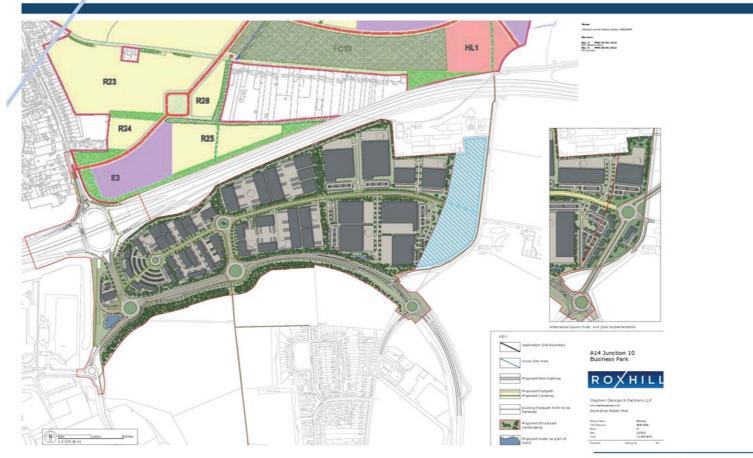

Illustrative Masterplan



